ID	Task Name	Duration	Start	Finish	Resource Names
1	Choose Groups	1 day	Wed 9/10/14	Wed 9/10/14	PM
2	Develop Functional requirements	6 days	Thu 9/11/14	Thu 9/18/14	BA
3	Use Case Diagrams	6 days	Thu 9/11/14	Thu 9/18/14	BA
4	Develop Use Cases	5 days	Mon 9/22/14	Fri 9/26/14	BA
5	Develop Wireframes	10 days	Fri 9/19/14	Thu 10/2/14	UX
6	Develop Interaction Diagram	5 days	Mon 9/29/14	Fri 10/3/14	BA
7	Test Case Development	35 days	Mon 9/29/14	Fri 11/14/14	QA
8	Presentation	1 day	Wed 11/5/14	Wed 11/5/14	PM,BA,UX,QA,Dev,Client
9	Development	35 days	Fri 10/3/14	Thu 11/20/14	Dev
10	Functional Testing	15 days	Fri 11/21/14	Thu 12/11/14	QA
11	Bug Fixing	15 days	Fri 11/21/14	Thu 12/11/14	Dev
12	Client Acceptance	1 day	Fri 12/12/14	Fri 12/12/14	Client,QA
13	Final Presentation (TBD)	1 day	Wed 12/10/14	Wed 12/10/14	PM,BA,UX,QA,Dev,Client

Project: Timeline.mpp
Date: Wed 9/24/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

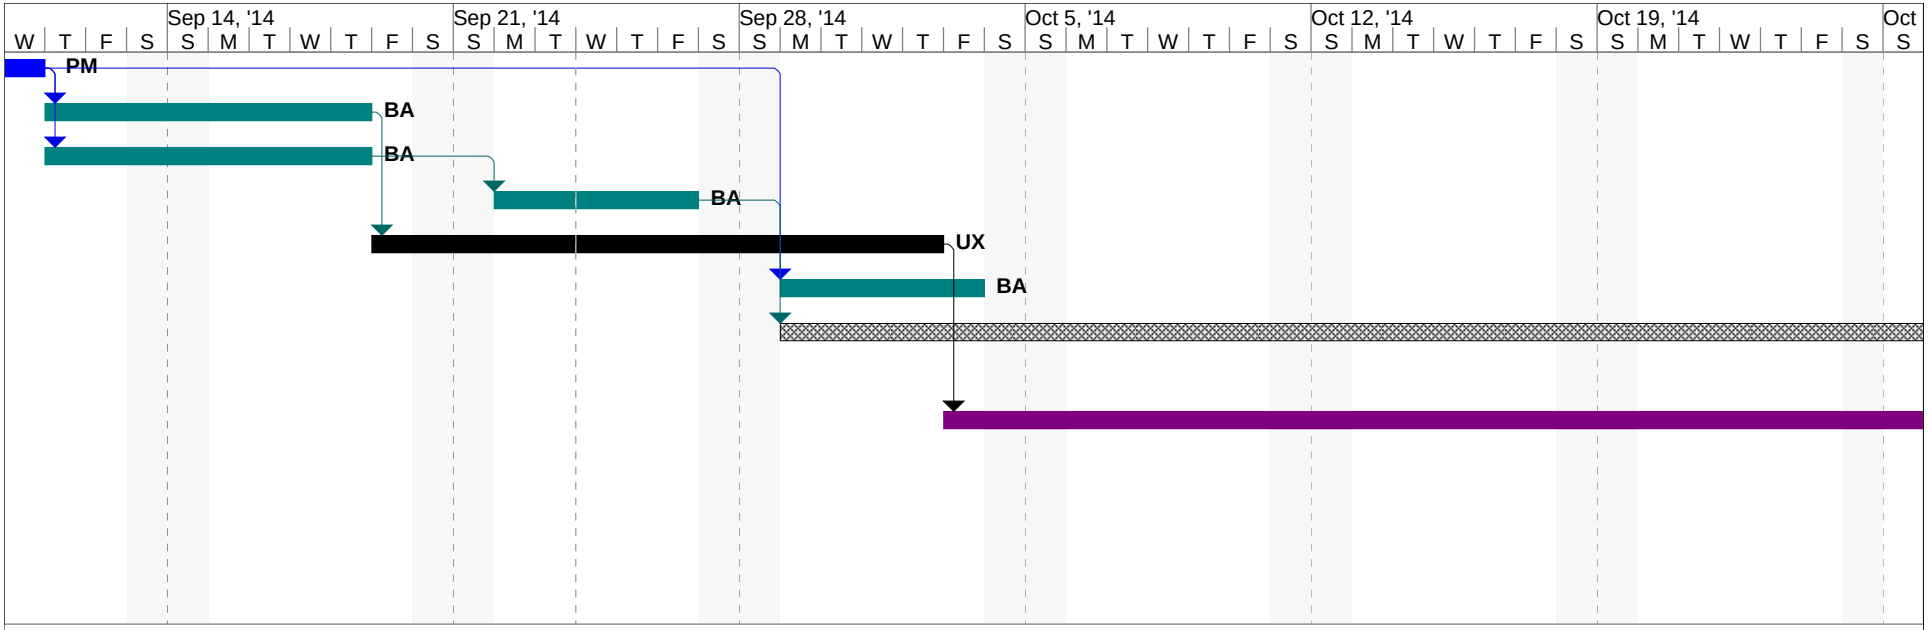

Project: Timeline.mpp
Date: Wed 9/24/14

Task	External Milestone	Manual Summary Rollup
Split	Inactive Task	Manual Summary
Milestone	Inactive Milestone	Start-only
Summary	Inactive Summary	Finish-only
Project Summary	Manual Task	Progress
External Tasks	Duration-only	Deadline

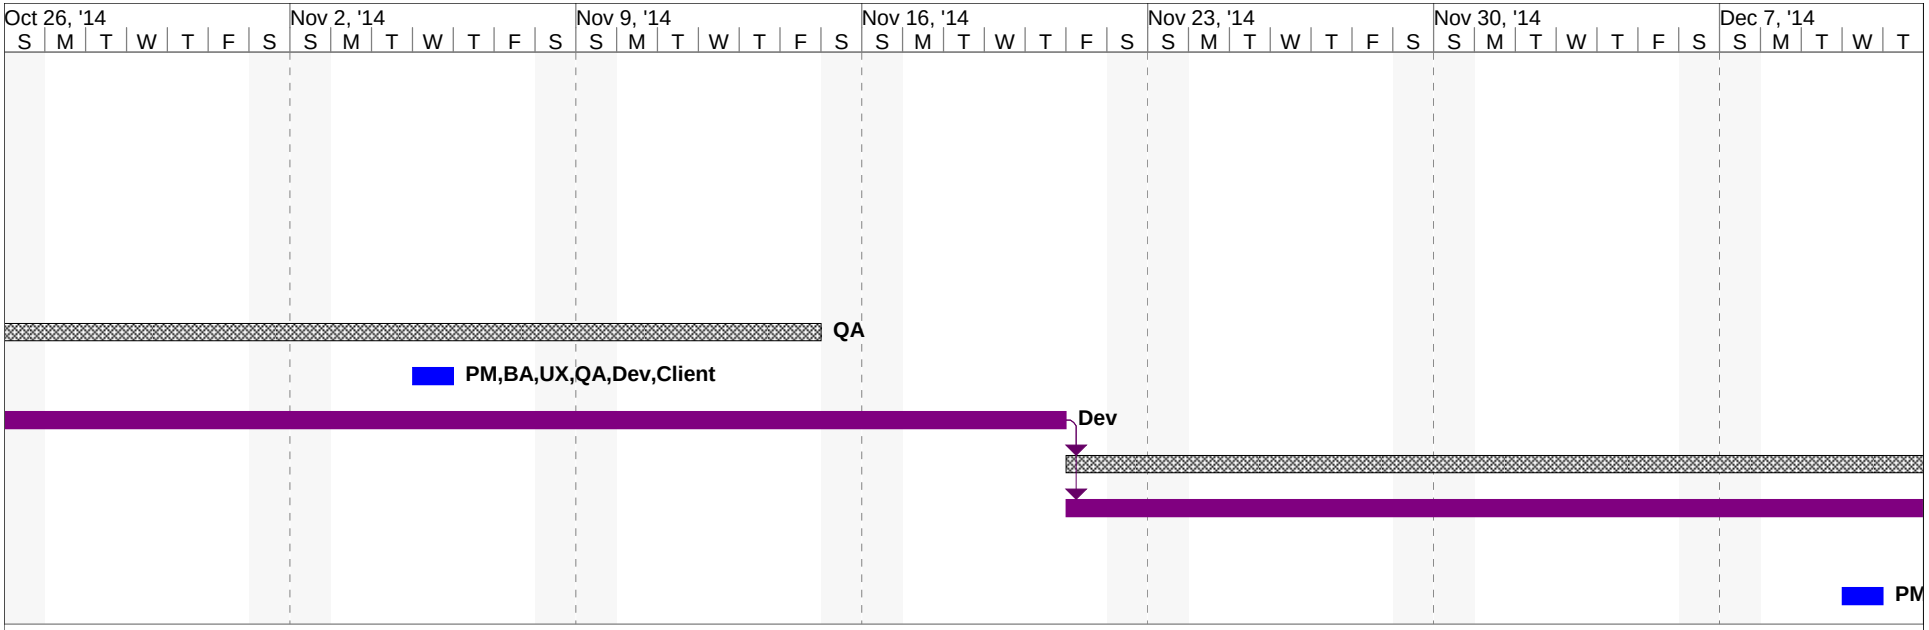

Project: Timeline.mpp
Date: Wed 9/24/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

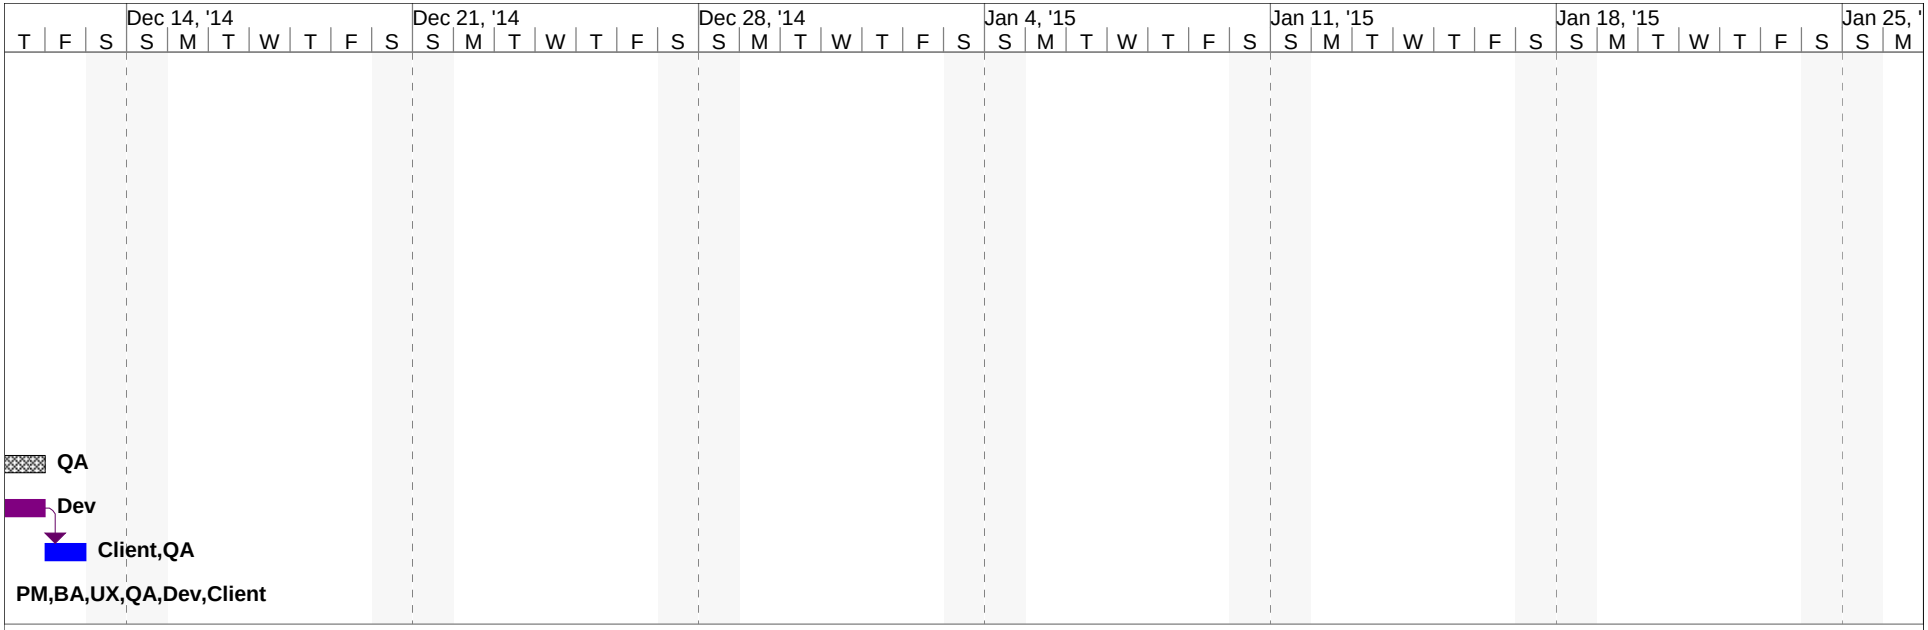

Project: Timeline.mpp
Date: Wed 9/24/14

Task	External Milestone	Manual Summary Rollup
Split	Inactive Task	Manual Summary
Milestone	Inactive Milestone	Start-only
Summary	Inactive Summary	Finish-only
Project Summary	Manual Task	Progress
External Tasks	Duration-only	Deadline
